



California Wildfire Mitigation Program

Monthly Status Report
August 2026

Last Updated August 13, 2026, 10:2...



Contents

California Wildfire Mitigation Program Overview	3
Section 1 Local Program Partners	4
Sections 2 - 3 Funding Source Payments Completed	5
Sections 4 - 5 Total Homes Application Information	6
Sections 6 - 7 Cost Share by AMI Bracket Homeowner Income Bracket	7
Sections 8 - 9 Social Vulnerabilities of Occupants Structure Type	8
Section 10 Cost Totals to Date	9
Section 11 Cost Totals by Category to Date	10
Sections 12 - 13 Cost Average Totals per Site Cost Total Averages by Category	11
Section 14 Community Reviewed Applications by Stage	12
Section 15 Issue and No Issue	15
Section 16 Closed Applications by Reason	16
Section 17 Local Program Partner Updates	17
Section 18 Awaiting Action	23

Report Notes

- Figures in this report are based on information reported by participating Local Program Partner.
- Unless otherwise noted, application-related figures are relative to active applications.
- Some tables are limited to subrecipient-reviewed active applications based on the data source.
- Siskiyou is a State-only funded project focused primarily on defensible space and Zone 0.
- Cost figures reflect site work financial data submitted by Local Program Partner to date and do not represent all expenditures incurred by the communities.



California Wildfire Mitigation Pilot Program Overview

In 2019, the California Legislature passed [Assembly Bill 38 \(Wood\)](#), Statutes of 2019, Chapter 391, directing the California Governor's Office of Emergency Services (Cal OES) and the Department of Forestry and Fire Protection (CAL FIRE) to enter into a [Joint Powers Agreement \(JPA\)](#) to develop and administer the **California Wildfire Mitigation Program (CWMP)**. As of 2026, Assembly Bill 1531 expanded the JPA Board to include the California Department of Insurance. The program was established to harden homes and create defensible space in high risk and socially vulnerable communities. In response, the agencies formed the California Wildfire Mitigation Program Authority (CWMPA) in December 2021 and appointed its Board of Directors in June 2022. Since hiring an Executive Director and staff and launching operations in 2022, the CWMPA has made significant progress in advancing this mission.

The California Wildfire Mitigation Program Authority is tasked with developing and administering a comprehensive wildfire mitigation program that accomplishes both of the following:

- **Encourages cost-effective structure hardening and retrofitting** to create fire-resilient homes, businesses, and public buildings at a communitywide scale.
- **Facilitates vegetation management**, including the creation and maintenance of the state-mandated 100 feet of defensible space.

Additionally, in coordination with state and local partners, the CWMP is establishing a statewide wildfire home-hardening framework that can be modeled across California communities. This framework enables communities to leverage state and federal resources to develop local wildfire home-hardening programs tailored to their resilience needs. To help accelerate local program development and inform the build-out of the statewide framework, the CWMPA provides state funding, resources, and support to demonstration communities implementing home-hardening projects in areas with high social vulnerability and wildfire risk.

Mitigation planning and project implementation are the only sustainable path to breaking the cycle of disaster damage, reconstruction, and repeated loss. To protect communities from catastrophic wildfires, it is essential for State and Federal partners to invest in mitigation activities not only at the landscape scale—where forest health and fuels reduction are critical—but also at the community scale, where wildfire-hardening homes and establishing defensible space are equally vital. These interventions work together to change wildfire behavior, reduce fire intensity, and significantly mitigate losses from destructive wildfire events.

California Wildfire Mitigation Program Authority

J. Lopez, Executive Director

Mobile: (916) 291-7159

Email: LopezJ4@caloes.ca.gov

[California Wildfire Mitigation Program Authority](#)

[California Wildfire Mitigation Program | OSFM](#)




1. Local Program Partners

The CWMPA has established local FEMA HMGP programs in San Diego, Shasta, Lake, Tuolumne, and El Dorado Counties, with program development underway in Siskiyou and Riverside Counties. These counties were prioritized as potential demonstration areas following a statewide analysis of parcels and census tracts with high wildfire hazard and high social vulnerability. The analysis incorporated fire hazard data, climate-related risk factors, and census indicators. Within each county, project areas were selected with input from local representatives, drawing on their on-the-ground expertise, and were required to be areas at elevated wildfire risk with high concentrations of socially vulnerable residents.

CWMP participating communities submitted Hazard Mitigation Grant Program (HMGP) subapplications to the Federal Emergency Management Agency (FEMA). Three communities Lake, Shasta, and San Diego Counties, submitted in fall 2021, followed by Tuolumne and El Dorado Counties in early 2022. The Siskiyou County project in West Mount Shasta is a State-only funded project that focuses primarily on defensible space and Zone 0. The intent of the CWMP Pilot is to retrofit more than 2,000 homes at the neighborhood and community scale by 2029.

Local Program Partner	County	Project Area(s)
North Coast Opportunities, Inc.	Lake	Kelseyville Riviera
San Diego County Fire Protection District	San Diego	Dulzura, Campo, Potrero
Shasta County Fire Safe Council	Shasta	Whitmore, Oak Run, Lakehead
Shasta Valley Resource Conservation District	Siskiyou	West Mount Shasta
El Dorado County Office of Wildfire Preparedness and Resilience	El Dorado	Weber Creek
Tuolumne County Office of Emergency Services	Tuolumne	Ponderosa Hills, Mira Monte, Sunrise





2. Funding Source

Cal OES administers the Federal Emergency Management Agency (FEMA) Hazard Mitigation Grant Program (HMGP) for the State of California. HMGP is a post-disaster funding program that covers up to 75 percent of the cost of eligible mitigation projects. The CWMPA and Cal OES are working closely with FEMA to leverage the \$21.9 million in State funds allocated to the CWMP through the 2020 Budget Act to meet the required non-federal cost share for demonstration communities participating in HMGP. This approach maximizes available funding and increases the resources dedicated to creating defensible space and implementing wildfire home-hardening measures.

County	Disaster	Federal Match	FEMA POP End Date	Local Match	State Liquidation Date	State Match	Total Award
Lake	4482	\$19,964,277 (90%)	02/01/2027	\$0	06/30/2029	\$2,218,253 (10%)	\$22,182,530
San Diego	4558	\$17,646,450 (75%)	07/11/2027	\$0	06/30/2029	\$5,882,150 (25%)	\$23,528,600
Shasta	4569	\$17,656,600 (75%)	08/28/2026	\$0	06/30/2029	\$5,885,534 (25%)	\$23,542,134
Siskiyou	N/A	\$0	N/A	\$0	06/30/2029	\$3,598,000 (100%)	\$3,598,000
El Dorado	4482	\$22,380,345 (90%)	02/01/2027	\$1,208,539 (4.86%)	06/30/2029	\$1,278,166 (5.14%)	\$24,867,050
Tuolumne	4482	\$17,689,680 (90%)	02/01/2027	\$0	06/30/2029	\$1,965,520 (10%)	\$19,655,200

3. Payments Completed

County	Total Award	Total Payments	Percent Paid
Lake	\$22,182,530.00	\$3,564,019.80	16.07%
San Diego	\$23,528,600.00	\$2,352,860.00	10.00%
Shasta	\$23,542,134.00	\$4,187,214.00	17.79%
Siskiyou	\$3,598,000.00	\$1,852,849.60	51.50%
El Dorado	\$24,867,050.00	\$294,616.14	1.18%
Tuolumne	\$19,655,200.00	\$148,976.42	0.76%
Total	\$117,373,514.00	\$12,400,535.96	10.57%



4. Total Homes

County	In Progress Sites	Completed Sites
Lake	6	70
San Diego	4	30
Shasta	0	38
Siskiyou	10	44
El Dorado	0	0
Tuolumne	0	0
Total	20	182

5. Application Information

County	Total Applications	Applications Pending Submission	Closed Applications	Active Applications
Lake	159	3	45	111
San Diego	262		99	163
Shasta	186		47	139
Siskiyou	111	1	16	94
El Dorado	56	2	6	48
Tuolumne	111	2	6	103
Total	885	8	219	658

Sites Assessed

471

Total

Sites in Progress

20

Total

Sites Completed

182

Total

Sites Completed in 2024

11

Sites Completed in 2025

107

Sites Completed in 2026

64



6. Cost Share by AMI Bracket

This innovative program is designed to eliminate barriers that have historically prevented disadvantaged communities from undertaking mitigation activities and to incentivize wildfire home hardening and defensible space in the most socially vulnerable, highest-risk areas. The program incorporates a “community hardening” strategy that strengthens entire neighborhoods, rather than supporting only scattered homeowners who already have the means to harden their homes. To encourage broad neighborhood participation, the program covers the full cost of retrofit and defensible space implementation, upwards of \$40,000, for homeowners earning up to 120 percent of the area median income. At the same time, CWMP is structured to work with all community members and includes established income guidelines for participation. Please see the chart below.

In accordance with the requirements established by AB 38, the primary goal of the CWMP is to provide financial assistance to underserved populations in wildfire-prone areas throughout California. In addition to offering financial support, the CWMP delivers educational resources on wildfire home hardening and defensible space, as well as technical assistance to help communities implement the program at the local level. Through this work, the California Wildfire Mitigation Program Authority aims to drive systemic change in wildfire preparedness, advancing communitywide, long-term resilience.

AMI Income Bracket	120% or less	Greater than 120% - 200%	Greater than 200%
Homeowner Cost Share	0%	10%	25%
Cap Per Resolution 2025-03	\$0	\$3,000	\$6,000

7. Homeowner Income Bracket

County	Less than 80%	80% through 120%	Above 120% to 200%	Greater than 200%
Lake	59	29	12	7
San Diego	94	43	11	1
Shasta	70	31	22	16
Siskiyou	30	11	26	20
El Dorado	15	15	11	7
Tuolumne	38	31	31	3
Total	306	160	113	54

- Based on Current Area Median Income (AMI) per California Department of Housing and Community Development (HCD)
- Cost Share begins after 120% AMI (Red line)



8. Social Vulnerabilities of Occupants

Natural disasters have historically had a disproportionate impact on communities with high concentrations of vulnerable populations, including people with lower socio-economic status, racial and ethnic minorities, older adults, individuals with disabilities, and others facing systemic barriers. These communities often encounter significant obstacles in accessing mitigation and recovery resources due to financial constraints, complex grant requirements, and other societal challenges. Socially vulnerable homeowners, in particular, face steep barriers to maintaining defensible space or implementing recommended wildfire home-hardening measures, with costs that can be prohibitive, such as a new roof that may exceed \$20,000. Because wildfire spreads easily between homes, entire neighborhoods must undertake home-hardening activities to effectively protect individual structures.

As a result, achieving true community resilience is often out of reach for socially vulnerable neighborhoods without targeted support and investment.

County	No Car	Has Disability	Preferred Language Other Than English	Age 5 or Under	Age 65 or Older
Lake	1	13	2	6	15
San Diego	1	44	8	19	45
Shasta	2	26	0	9	55
Siskiyou	0	8	0	2	27
El Dorado	1	14	0	5	28
Tuolumne	0	30	1	14	49
Total	5	135	11	55	219

9. Structure Type

County	Manufactured or Mobile Home	Multi Family Residence	Single Family Residence	Total
Lake	0	1	103	104
San Diego	13	0	127	140
Shasta	22	0	117	139
Siskiyou	2	1	84	87
El Dorado	0	0	0	0
Tuolumne	0	0	0	0
Total	37	2	431	470



10. Cost Totals to Date


As part of the program, CWMPA, Cal OES, and CAL FIRE staff provide guidance, technical assistance, and grant-management support to the demonstration communities as they plan and implement their projects. CWMPA and Cal OES have developed electronic platforms for homeowner applications in English and Spanish, as well as grant-management tools for use by local communities. CWMPA and CAL FIRE have also delivered technical support and training on property assessments and wildfire home-hardening measures to be implemented at homesites. These eligible measures are informed by the latest fire science—developed in collaboration with experts at the National Institute of Standards and Technology, the Insurance Institute for Business and Home Safety, and CAL FIRE—to mitigate risks from embers, radiant heat, and convective heat. In addition, CWMPA and CAL FIRE jointly created a mobile application to support the completion of home assessments, which inform site-specific scopes of work. CWMPA and Cal OES have also established a suite of implementation resources for communities, including customizable outreach materials, an implementation guide, and template federal applications.

This strategy promotes communitywide resiliency and maximizes the impact of wildfire-hardening efforts, reducing risk exponentially as neighboring homes are hardened together.

County	Grand Total	Construction Total	Defensible Space Totals
Lake	\$259,503,058.03	\$3,060,073.54	\$445,544.49
San Diego	\$1,629,248.12	\$1,435,900.34	\$193,347.78
Shasta	\$1,813,695.13	\$1,610,742.13	\$202,953.00
Siskiyou	\$853,042.80	\$2,619.30	\$850,423.50
El Dorado	\$0.00	\$0.00	\$0.00
Tuolumne	\$0.00	\$0.00	\$0.00
Total	\$263,799,044.08	\$6,109,335.31	\$1,692,268.77

**11. Cost Totals by Category to Date**

Cost Category	Lake	San Diego	Shasta	Siskiyou	Total
Accessory Buildings	\$37,198.96	\$14,716.03	\$46,600.00	\$0.00	\$98,514.99
Attachments	\$435,882.36	\$669,447.29	\$396,000.00	\$0.00	\$1,501,329.65
Doors	\$123,322.86	\$178,570.64	\$49,650.00	\$0.00	\$351,543.50
Exterior Coverings	\$964,617.08	\$134,911.75	\$354,710.00	\$0.00	\$1,454,238.83
Miscellaneous Structures	\$29,130.06	\$8,699.16	\$6,000.00	\$0.00	\$43,829.22
Roofs	\$258,157.62	\$139,610.80	\$162,219.63	\$0.00	\$559,988.05
Vents	\$308,898.90	\$107,247.76	\$108,210.00	\$0.00	\$524,356.66
Windows	\$124,772.56	\$67,147.85	\$150,075.00	\$0.00	\$341,995.41
Other Expenses	\$778,093.14	\$115,549.06	\$337,277.50	\$2,619.30	\$1,233,539.00
Defensible Space	\$445,544.49	\$193,347.78	\$202,953.00	\$850,423.50	\$1,692,268.77
Total	\$3,505,618.03	\$1,629,248.12	\$1,813,695.13	\$853,042.80	\$7,801,604.08

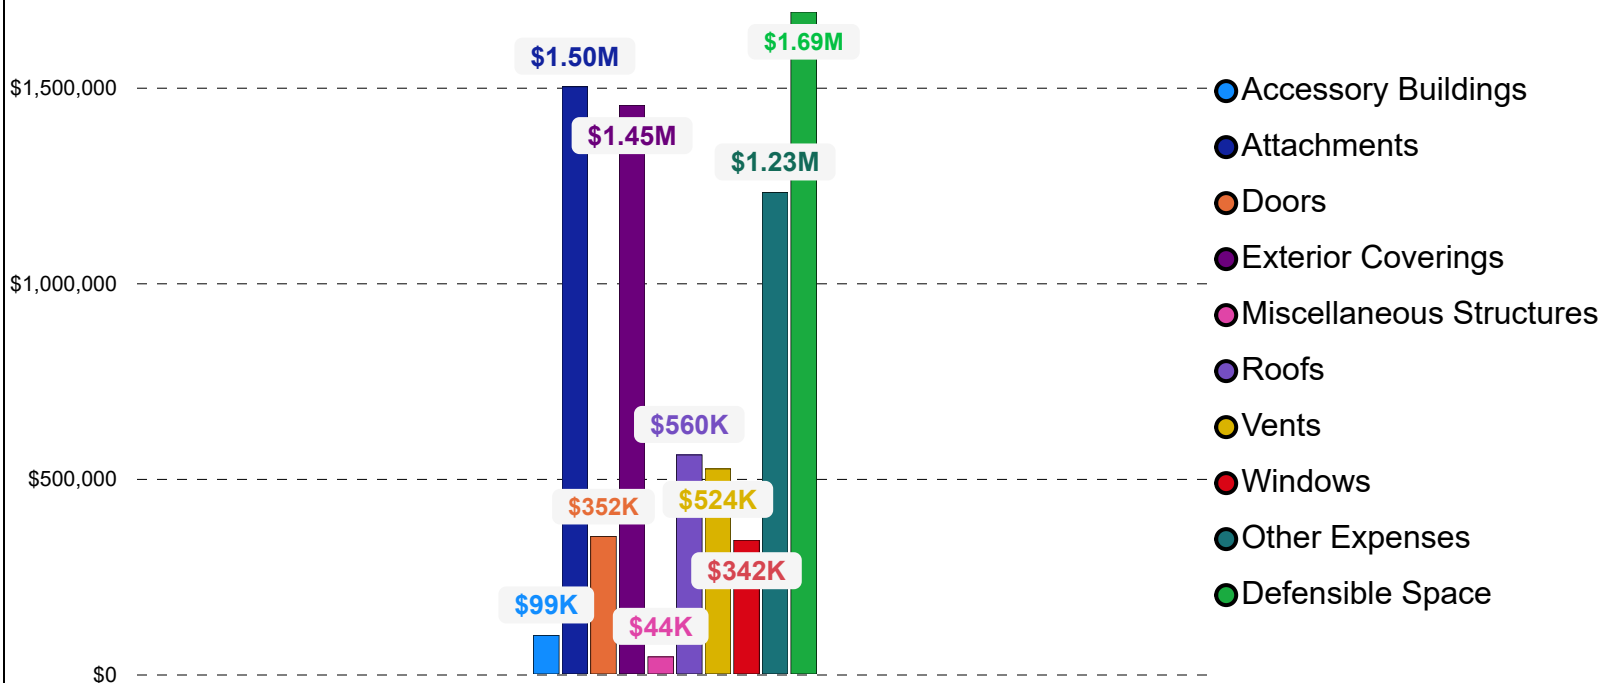Cost Totals Graph

- Siskiyou project area focused primarily on defensible space and Zone 0
- All figures reflect site work financial data submitted by Local Program Partner to date, and does not represent all expenditures incurred by the communities

**12. Cost Average Totals per Site**

County	Construction Total	Defensible Space Total	Grand Total
Lake	\$45,672.74	\$6,649.92	\$3,873,179.97
San Diego	\$62,430.45	\$8,406.43	\$70,836.87
Shasta	\$43,533.57	\$5,485.22	\$49,018.79
Siskiyou	\$109.14	\$35,434.31	\$35,543.45
El Dorado	\$0.00	\$0.00	\$0.00
Tuolumne	\$0.00	\$0.00	\$0.00
Total	\$40,459.17	\$11,207.08	\$1,747,013.54

- Shows the average total cost per home/site by county.
- This may not equal the sum of category averages because each category is averaged separately.

13. Cost Total Averages by Category

Cost Category	Lake	San Diego	Shasta	Siskiyou
Accessory Buildings	\$2,479.93	\$2,452.67	\$4,236.36	\$0.00
Attachments	\$6,810.66	\$29,106.40	\$16,500.00	\$0.00
Defensible Space	\$6,649.92	\$9,207.04	\$5,637.58	\$35,434.31
Doors	\$1,957.51	\$7,763.94	\$1,460.29	\$0.00
Exterior Coverings	\$16,349.44	\$6,745.59	\$11,084.69	\$0.00
Miscellaneous Structures	\$3,236.67	\$2,174.79	\$1,000.00	\$0.00
Roofs	\$3,911.48	\$6,345.95	\$7,724.74	\$0.00
Vents	\$4,752.29	\$4,662.95	\$3,279.09	\$0.00
Windows	\$1,919.58	\$2,919.47	\$6,253.13	\$0.00
Other Expenses	\$11,613.33	\$5,252.23	\$9,919.93	\$2,619.30
Total	\$59,680.81	\$76,631.02	\$67,095.82	\$38,053.61


- Shows the average cost for each category when that category had a cost
- \$0 values are excluded from the average




14. Community Reviewed Applications by Stage

Each demonstration community has a lead implementing agency responsible for tailoring the program to best meet the needs of its project areas. The local implementing agency manages the day-to-day delivery of the program throughout its lifecycle, including conducting homeowner outreach; receiving and reviewing homeowner applications, completing home assessments to identify the most impactful defensible space and retrofit measures based on each home's unique characteristics; and coordinating with contractors and building officials to carry out the approved scope of work.

Lake Reviewed Applications by Stage

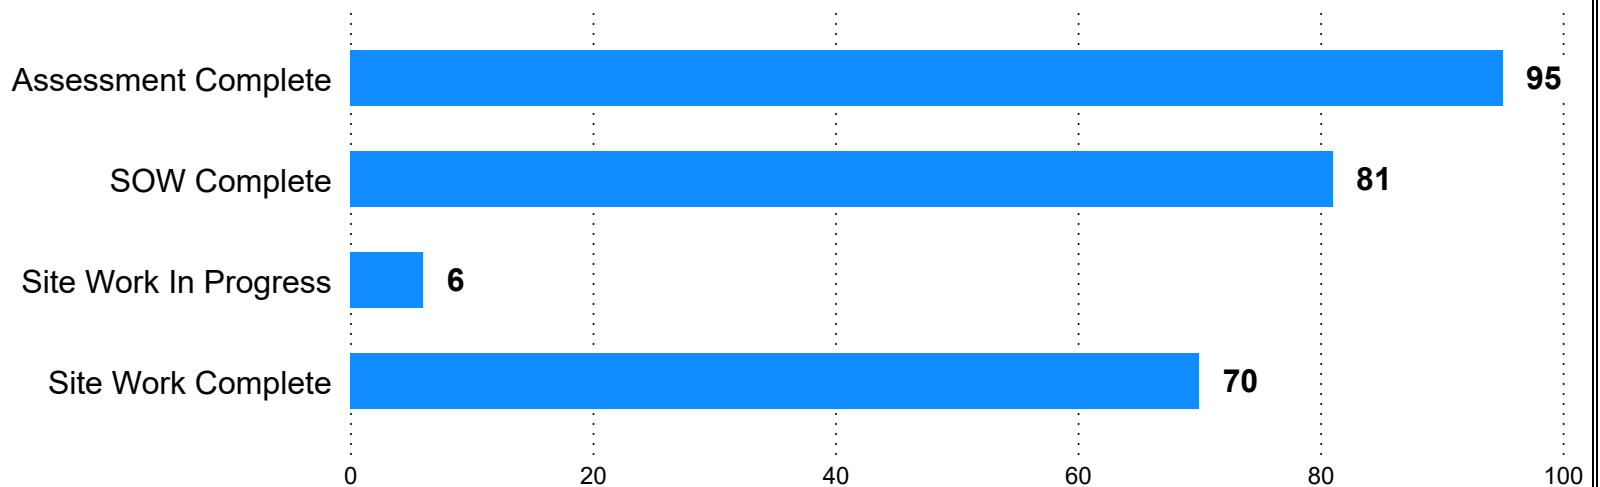


San Diego Reviewed Applications by Stage

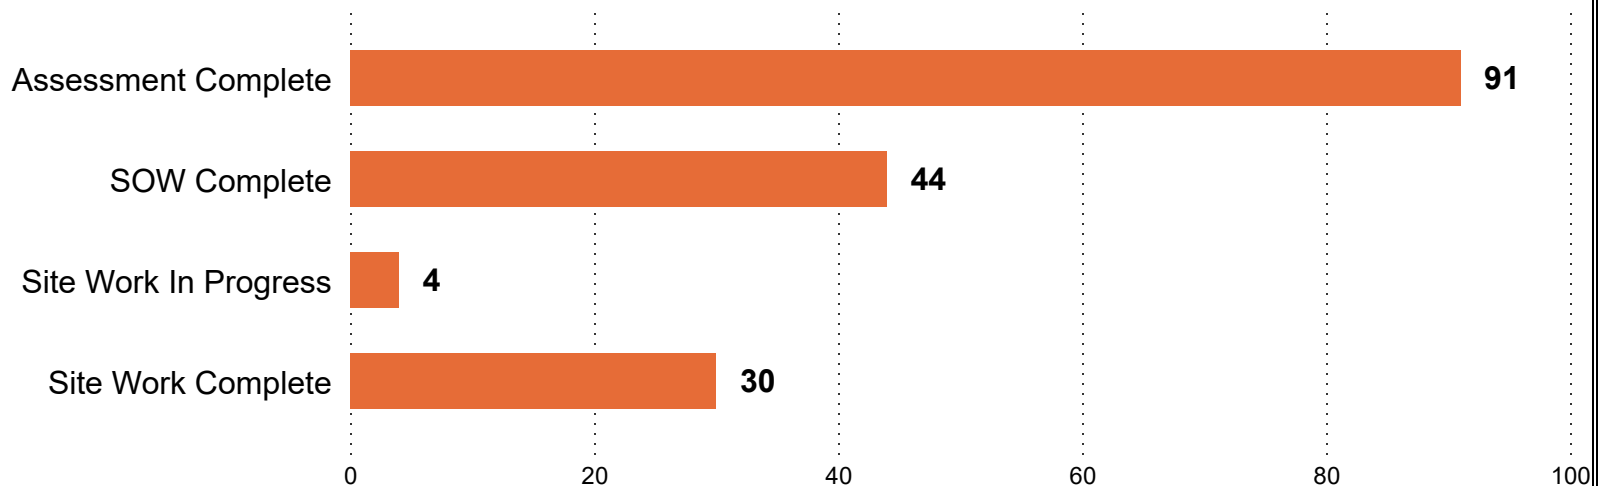





Shasta Reviewed Applications by Stage

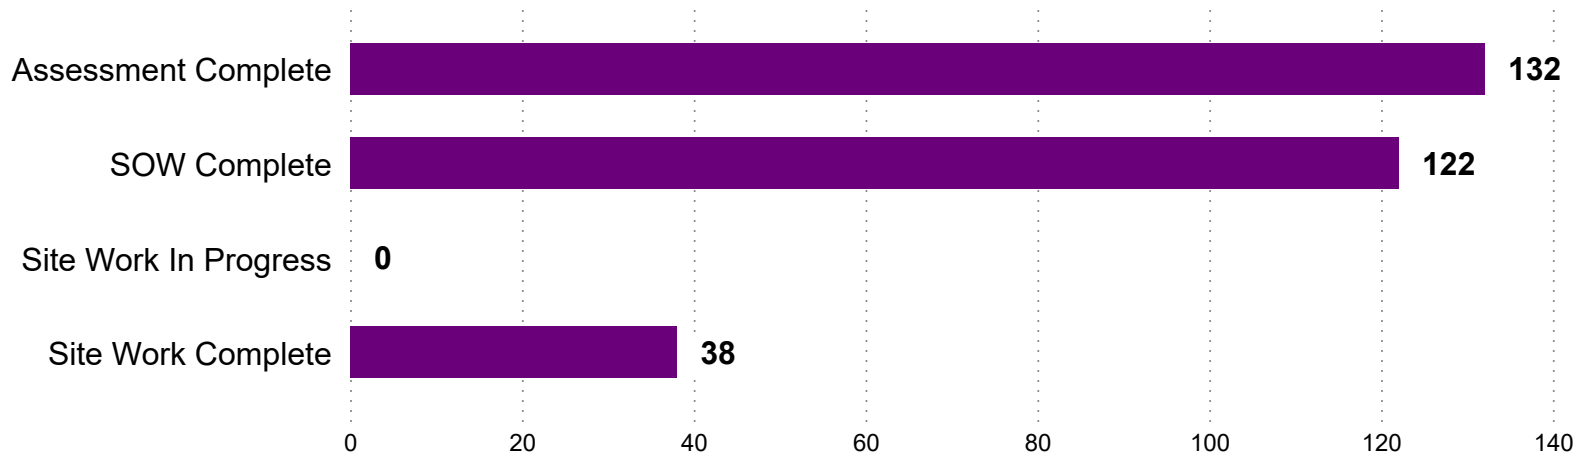

Siskiyou Reviewed Applications by Stage

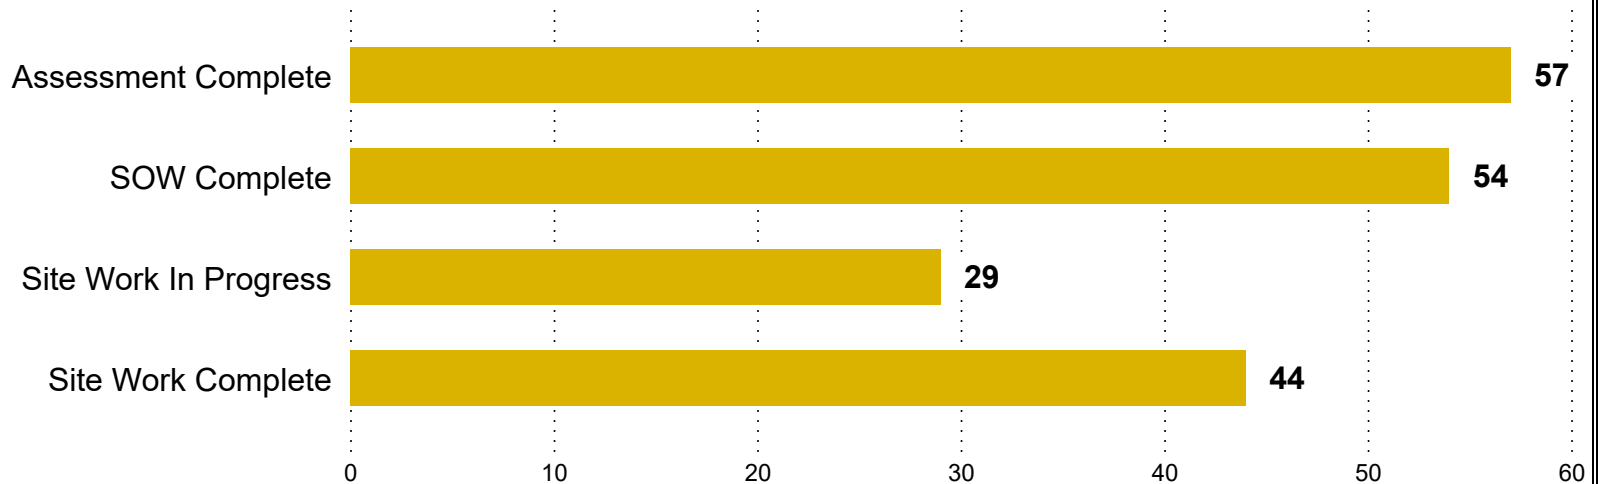


Tuolumne Reviewed Applications by Stage

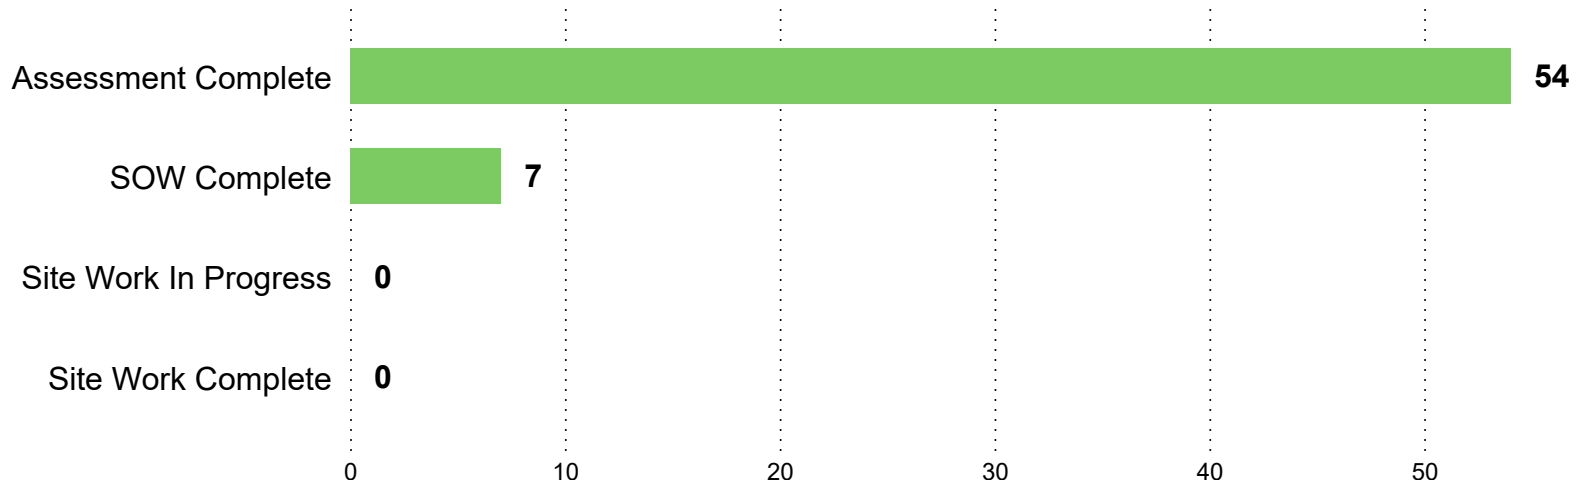




El Dorado Reviewed Applications by Stage

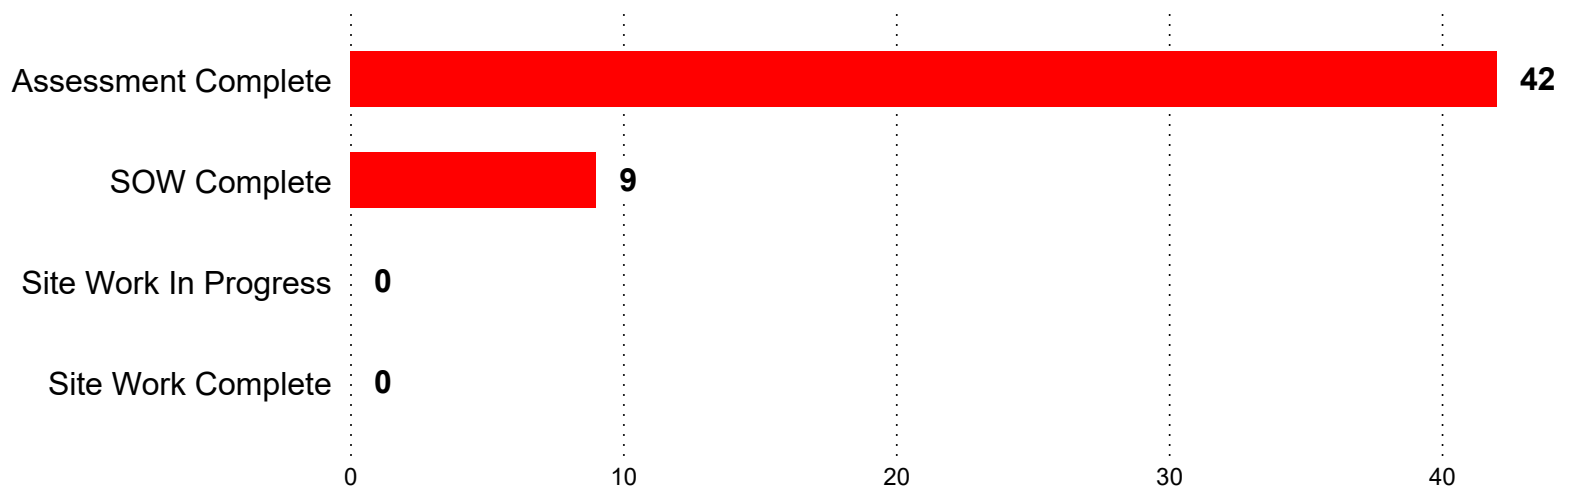


Total Reviewed Applications by Stage

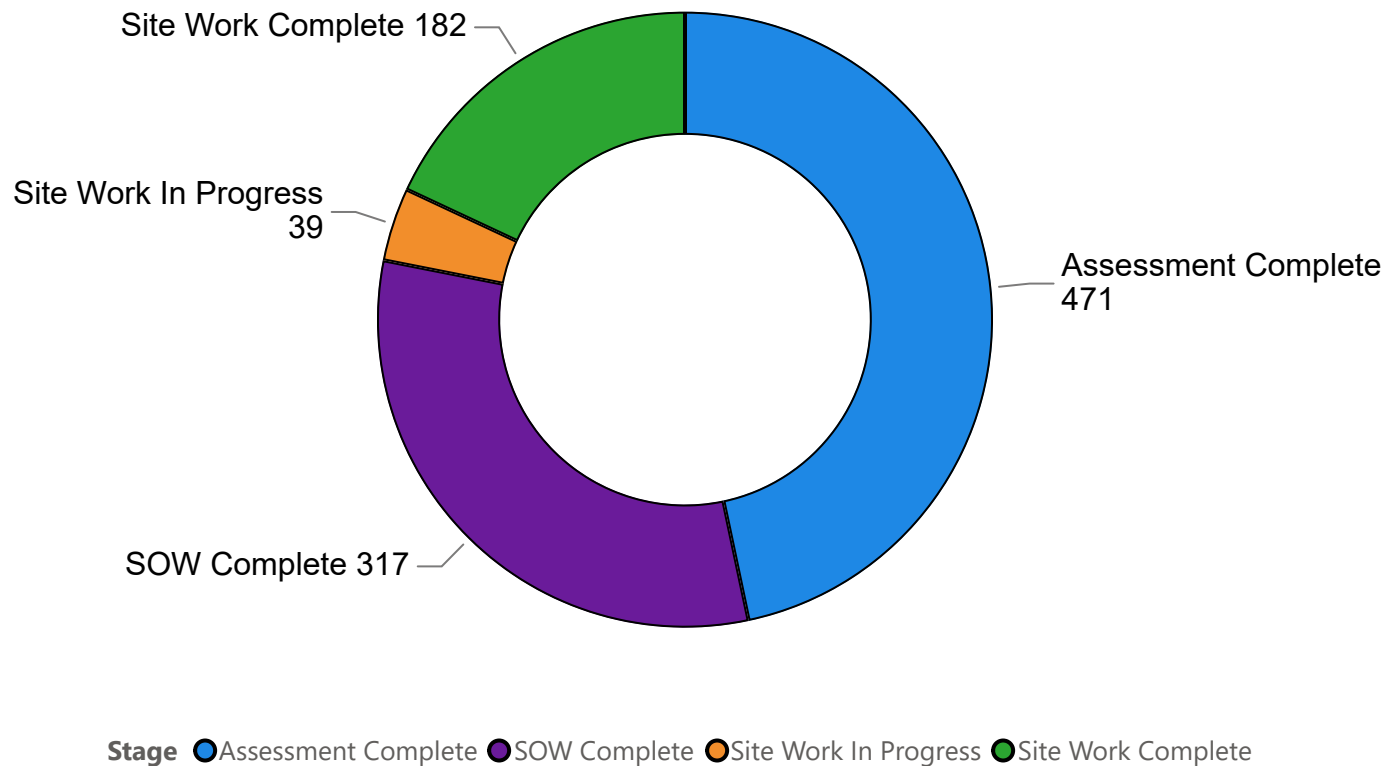



15. Issue and No Issue

As part of the program, CWMPA, Cal OES, and CAL FIRE staff provide guidance, technical assistance, and grant-management support to the demonstration communities as they plan and implement their projects. CWMPA and Cal OES have developed electronic platforms for homeowner applications in English and Spanish, as well as grant-management tools for use by local communities. CWMPA and CAL FIRE have also delivered technical support and training on property assessments and wildfire home-hardening measures to be implemented at homesites. These eligible measures are informed by the latest fire science—developed in collaboration with experts at the National Institute of Standards and Technology, the Insurance Institute for Business and Home Safety, and CAL FIRE—to mitigate risks from embers, radiant heat, and convective heat. In addition, CWMPA and CAL FIRE jointly created a mobile application to support the completion of home assessments, which inform site-specific scopes of work. CWMPA and Cal OES have also established a suite of implementation resources for communities, including customizable outreach materials, an implementation guide, and template federal applications.

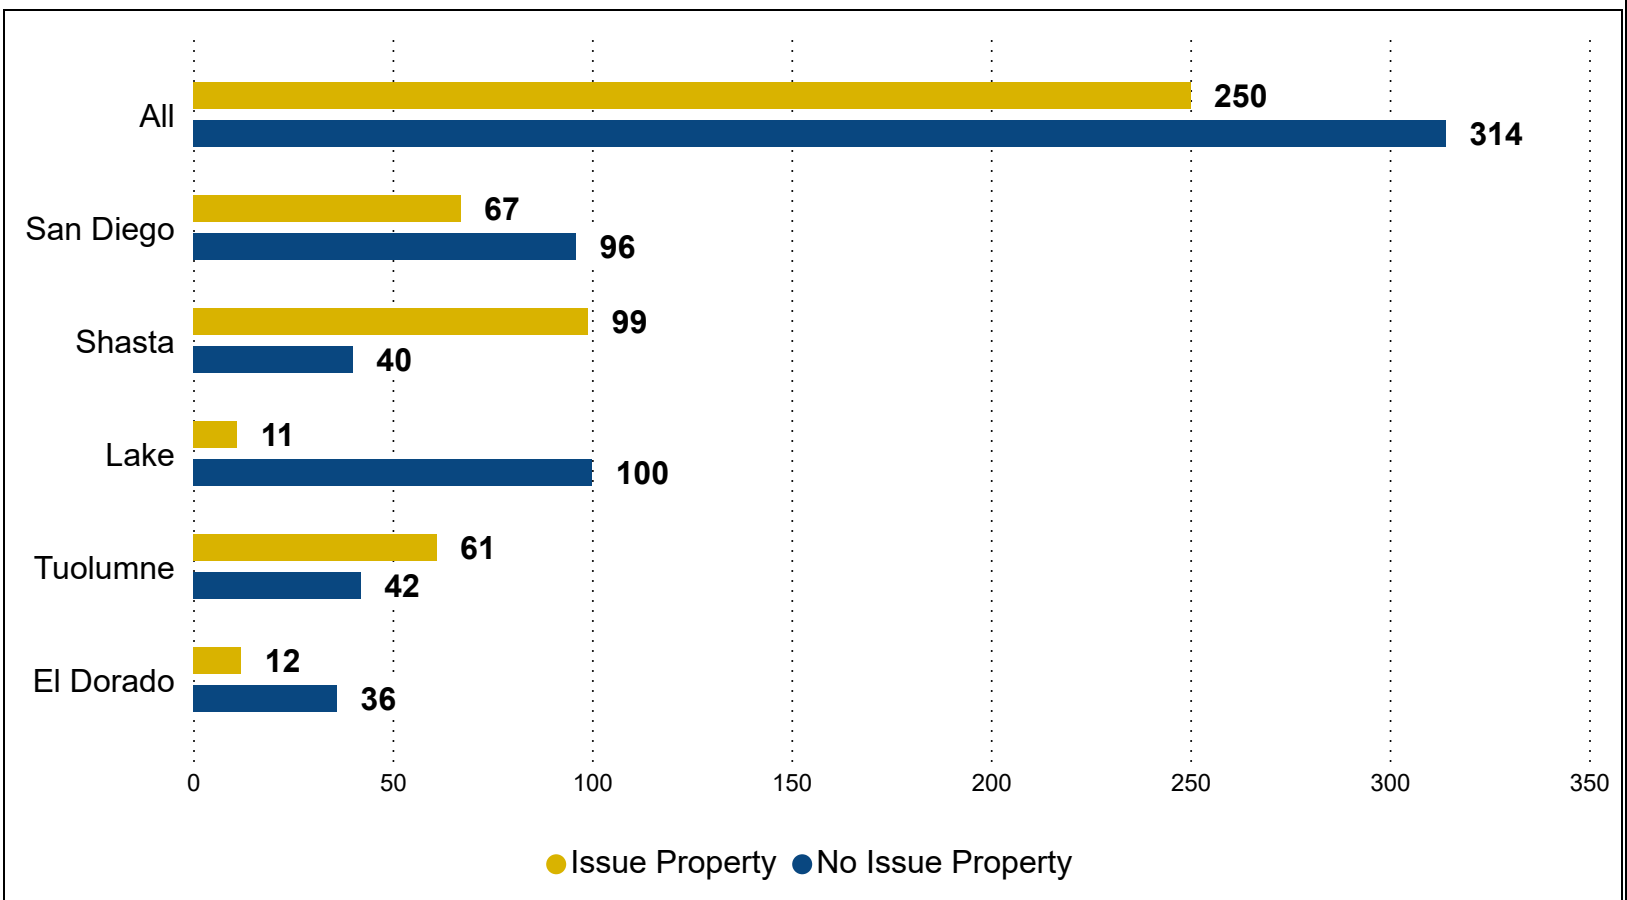


- Issue and No Issue status does not apply to non-federally funded projects, such as Siskiyou




16. Closed Applications by Reason

Rejected Applications

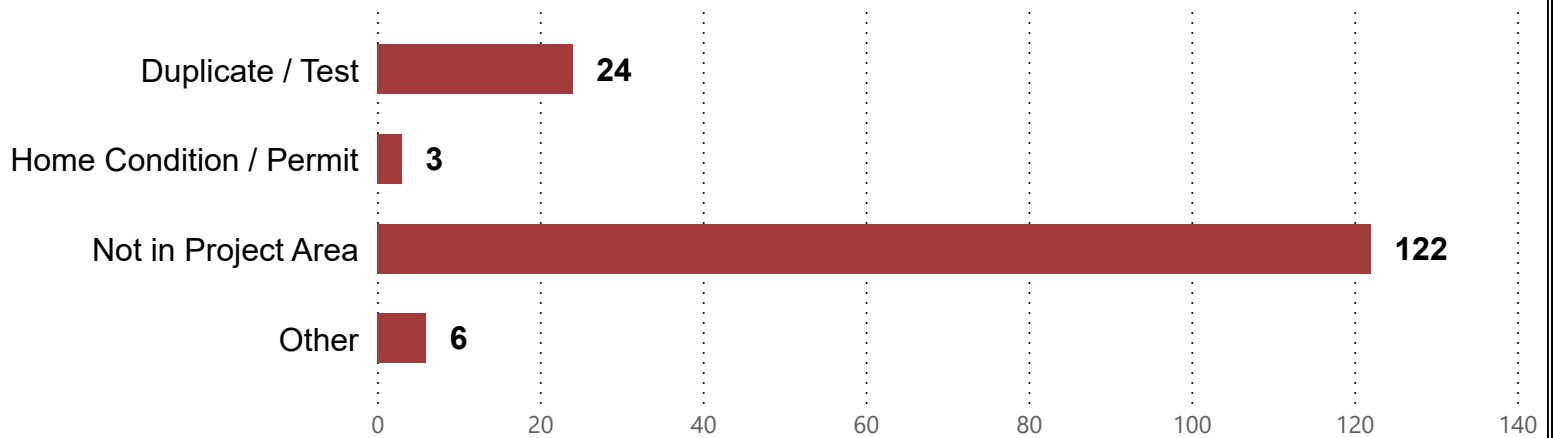

- Rejected Applications are initiated by Local Program Partner.

Withdrawn Applications

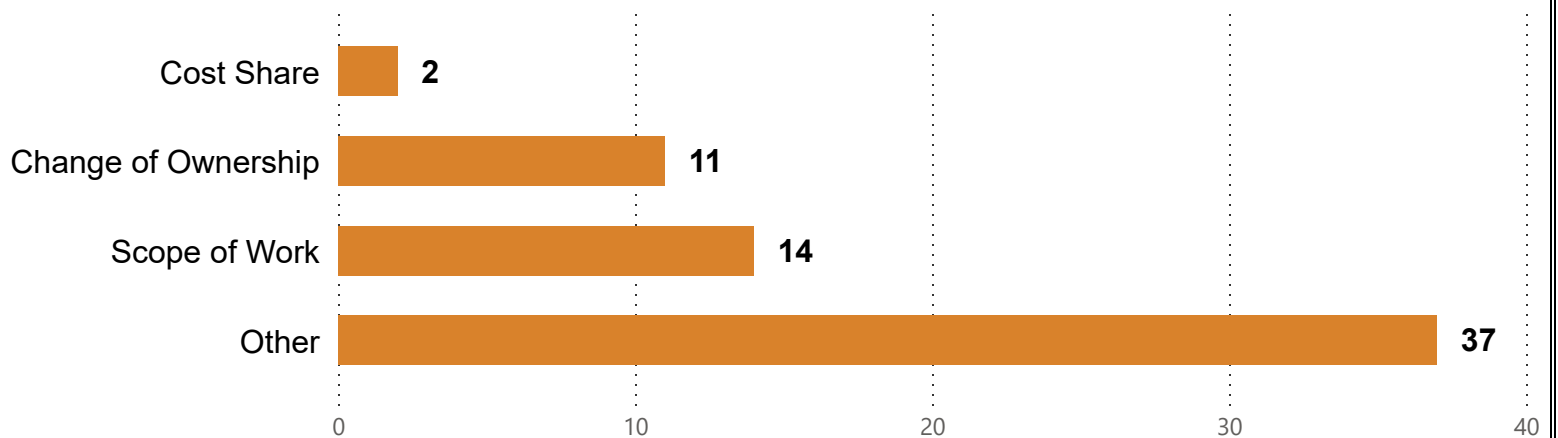

- Withdrawn Applications are initiated by Homeowner



17. Local Program Partner Updates

North Coast Opportunities in Lake County:

FEMA Award: 03/17/2023, Revised Award: 08/15/2023, DR 4482-PJ0514, POP End Date 02/01/2027

County	Total Applications	Pending Applications	Rejected or Withdrawn	Active Applications
Lake	159	3	45	111

EHP:

- 1,100 no issue parcels in the project area

Staffing and Contractors:

- 46 Total Qualified Contractors
- 3 Full time home assessors
 - All Assessors have been certified by CAL FIRE

Assessments and Site Work Progress:

- Homes in Progress: 6
- Assessors are moving at a consistent pace and are completing assessments faster than contractors are able to complete the homes.
- Plan to complete 2 SOW every other Tuesday.
 - Goal to complete 6 homes per month
- Completed Homes: 70

Program Documents:

- Documents development since 2023
- Finalization of the Master Agreement to Procure Contractors
- Finalization of Tri-Party Agreements
- SOW document and alignment with MQS documents

Project Activities / Misc. Info:

- NCO sends out a monthly newsletter with program updates to interested parties
 - Over 300 recipients
- NCO POP extension has been approved from 3/17/2026 to 2/1/2027.
- A homeowner has completed the IBHS home designation process and is ready for the final on-site inspection.
 - IBHS sent the homeowner a green light for the final site inspection which may be completed by NCO



San Diego County Fire Protection District in San Diego County:

FEMA Award: 08/29/2023: DR 4558-PA0800, POP End Date 07/11/2027

County	Total Applications	Pending Applications	Rejected or Withdrawn	Active Applications
San Diego	262		99	163

EHP:

- Development of the Phase II EHP reports; collaborating with SMEs and FEMA to develop a reporting standard to implement throughout other communities.
- Biological Assessment approved for all three project areas, Dulzura, Campo, and Potrero, including the expanded areas.

Staffing and Contractors:

- 7 County Prevention Specialists (Will be assisting with assessments), 5 County Building Inspectors for (Permitting purposes), 3 San Diego Fire Personnel (Observers)
- 4 contractors on the pre-qualified list
- 3 General Contractors, 1 Manufactured Home (C-47)
- Quarterly RFQ for more Contractors reopen every, February, May, August, and November
- Contract amendments have been executed so all contractors can work on Manufactured Homes

Assessments and Site Work Progress:

- 30 homes complete
- Three homes in progress
- Six homes in Tri-party agreement stage
- Four closeouts completed week of August 10

Program Documents:

- Finalization of the Tri-Party Agreement, and Master Agreement to Procure contractors.

Project Activities / Misc. Info:

- Pending REC for additional no issue properties
- Pending EHP Phase II for Campo Hills Issue Sites
- 8 have been submitted to FEMA and are under review

**Shasta County Fire Safe Council in Shasta County:**

FEMA Award: 08/28/2023, DR 4569-PA0974, POP End Date 08/28/2026

County	Total Applications	Pending Applications	Rejected or Withdrawn	Active Applications
Shasta	186		47	139

EHP:

- 144 total No-Issue parcels in Shasta County project area
 - 47 in Whitmore, 37 in Lakehead, 60 in Oak Run

Staffing and Contractors:

- Current Assessors on staff (or with WSRCD):8 total
- 36 Contractors on the pre-qualified list:
 - 14 General Contractors
 - 22 Defensible Space Contractor
- Part-time project assistant to assist with logistics, documents, contracts, SME coordination, etc.
- Signed a contract with outside DSpace project coordinator to assist with overseeing and inspecting DSpace work and to assist with SOWs.

Assessments and Site Work Progress:

- 38 Homes Completed
- Preparing bid walks and SOW for parcels to utilize state only funding.

Project Activities / Misc. Info:

- The Shasta team has stopped accepting new applications due to limited remaining project funding. The number of homes currently in the backlog exceeds the number that can likely be completed with the available funds.
- Preparing for Closeout, POP end date 8/28/2026 –
 - Existing procurement records will be reviewed with SPU to determine what must be uploaded
 - Developing strategies for State Only Funding
 - The project will continue using the current 75/25 funding through August 28, 2026, then transition to State-only funds
 - All available No-Issue homes have been completed

**Shasta Valley Resource Conservation District in Siskiyou County:**

Award: 05/01/2023, State Funds Only, CEQA, Defensible Space Only, POP End Date 06/30/2029

County	Total Applications	Pending Applications	Rejected or Withdrawn	Active Applications
Siskiyou	111	1	16	94

EHP:

- FEMA EHP is not applicable. SVRCD leveraged existing California Vegetation Treatment Program (CalVTP) for California Environmental Quality Act (CEQA) compliance.

Staffing and Contractors:

- 10 Contractors on pre-qualified List
- Current Assessor(s) in staff: 3. More to be trained in upcoming Assessor Training Class in mid-Spring.

Assessments and Site Work Progress:

- Batch One – 8 Homes – All work complete
- Batch Two - 7 Homes – All work complete
- Batch Three – 11 Homes – All work complete
- Batch Four – 9 Homes – All work complete
- Batch Five – 7 Homes – All work complete
- Batch Six – 3 Homes – All work complete
- Batch Seven – 3 Homes – All work complete
- Batches 8 & 9 have been awarded, working is in progress
- Batch Ten - 5 homes - Bid tour scheduled for 9/3/2026

Program Documents:

- Scope of work and Bid Form procedures complete.
- Tri-party Agreement has been finalized.
- SOW and Bid Forms were developed to meet CWMP standards as well as SVRCD existing processes and procedures.
- Contractor Procurement

Project Activities / Misc. Info:

- SVRCD goal to complete Defensible Space for approximately 100 parcels. 2-year period of performance.
- Modifying the Salesforce and Assessment App to conduct D-space only assessments.
- Modifying MQS to D-Space only.
- SVRCD has conducted training for participating contractors to teach the bidding process and explain the MQS.



Tuolumne County Office of Emergency Services:

FEMA Award: 6/22/2023 DR 4482-PJ00966, POP End Date 02/01/2027

County	Total Applications	Pending Applications	Rejected or Withdrawn	Active Applications
Tuolumne	111	2	6	103

Project Updates:

- The county is actively working on property assessments and developing their scopes of work.
- They are drafting tri-party, master agreements and CEQA Notice of Exemption.

Staffing and Contractors:

- One Analyst assisting with grant management.
- One full time project/construction manager.

Applications:

- 54 assessments have been completed.
- 7 completed and approved scopes of work

Project Activities / Misc. Info:

- The Office of Emergency Services has been absorbed into the Tuolumne County Sheriff's office.
- Door-to-door outreach was completed targeting homeowners who have applied within strategically clustered areas to maximize fire safety impact.
- CWMP and CAL FIRE continue review of the published scopes of work on a monthly basis, ensuring satisfactory implementation.



El Dorado County Office of Wildfire Preparedness and Resilience:

FEMA Award: 6/29/2023, DR 4482-PJ0796, POP End Date 02/01/2027

County	Total Applications	Pending Applications	Rejected or Withdrawn	Active Applications
El Dorado	56	2	6	48

Project Updates:

- The county is actively working on property assessments and developing their scopes of work.
- The RFQ for contractors resulted in 12 Defensible Space contractors and 4 Home Hardening contractors.
- They are finalizing tri-party and master agreements and presenting contractors to their board on 8/25/26.

Staffing and Contractors:

- Four defensible space inspectors for home assessments.
- Full time construction manager.

Applications:

- 40 assessments have been completed.
- 9 completed and approved scopes of work.

Project Activities / Misc. Info:

- The County and Construction Management firm has met with both County and City building and planning departments and designated queues have been established to streamline permitting processes for the project.
- Door-to-door outreach began, targeting homeowners who have applied within strategically clustered areas to maximize fire safety impact.
- CWMP and CAL FIRE continue review of the published scopes of work on a bi-weekly basis, ensuring satisfactory implementation.



18. Awaiting Action

Shasta Valley Resource Conservation District (SVRCD) in Siskiyou County

- Hazard Mitigation Grant Program
- Subapplication Submitted to FEMA November 21, 2024
 - 25% State Match \$5.7 million (Administration 5%)
 - 75% Federal Match \$17.1 million
 - Total funding: \$22.8 million
 - Community Level Program Impact: 400 to 500 homes

Riverside County

- Hazard Mitigation Grant Program
- Subapplication Submitted to FEMA November 21, 2024
 - 25% State Match \$6.6 Million (Administration 5%)
 - 75% Federal Match \$19.8 million
 - Total funding: \$26.4 million
 - Community Level Program Impact: 450 to 540 homes

SB-946, Personal Income Tax Law: Corporation Tax Law: exclusions: wildfire mitigation payments (2023-2024). **Applies to California Wildfire Mitigation Program applicants.**
